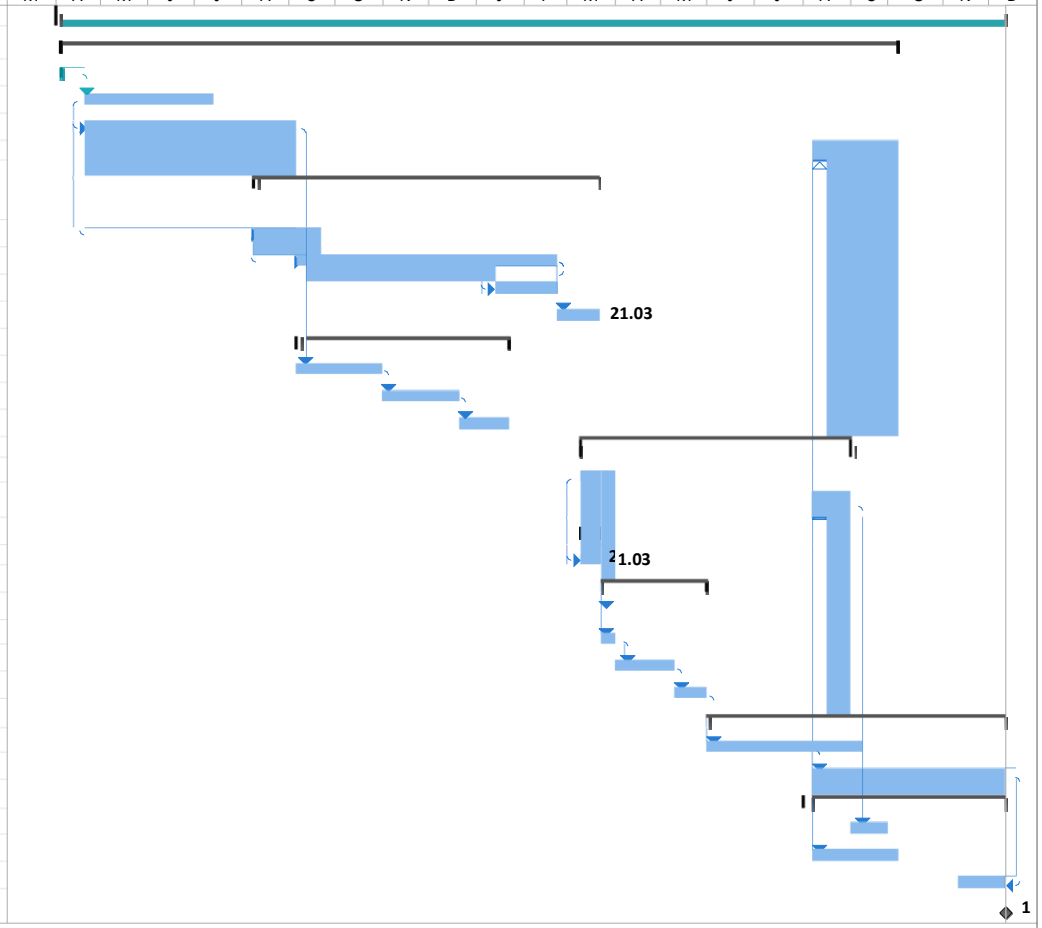ID	Task method	Task Name	Duration	Start	Finish	Previous tasks
1		**MANUFACTURING A NEW CRANE AND**	**40 days**	**Fri 5.04.24**	**Thu 11.12.25**	
2		**PREPARATION AND HAND-OVER OF**	**90 days**	**Fri 5.04.24**	**Thu 2.10.25**	
3		Contract signing	1 day		Fri 5.04.24	
4		Measurements on facility	60 days	on 22.04.24	Fri12.07.24	3KZ+10 days
5		Detailed design doc. prepar.	100 days	on 22.04.24	Fri 6.09.24	4SS
6		As-built doc. prepar.	40 days	Fri 8.08.25	Thu 2.10.25	27 7
		GANTRY CRANE MANUFACTURING WITH TRASH-RACK CLEANING MACHINE	**160 days**	**Mon 12.08.24**	**Fri 21.03.25**	
8		Material supply and control	30 days	on 12.08.24	Fri 20.09.24	5SS+80 days 9
		Manufacturing	120 days	Mon 9.09.24	Fri 21.02.25	8SS+20 days 10
		Corrosion protection of crane	30 days	on 13.01.25	Fri 21.02.25	9KZ-30 days
11		Testing at manufacturer	20 days	on 24.02.25	Fri 21.03.25	9 12
		LIFTING TONGS MANUFACTURING	**97 days**	**Mon 9.09.24**	**Tue 21.01.25**	13
		Material supply and control	38 days	Mon 9.09.24	Wed 30.10.24	
5						
14		Manufacturing of tongs	36 days	Thu 31.10.24	Thu 19.12.24	13
16		**RAMP ELEVATION**	**129 days**	**Mon**	**Thu 4.09.25**	
17		Ramp elevation at A2	20 days	Mon	Fri 4.04.25	
18		Ramp elevation at A1	20 days	Fri 8.08.25	Thu 4.09.25	27
19		**SUPPLY OF CRANE AND TONGS TO**	**10 days**	**Mon**	**Fri 21.03.25**	
20		Supply of crane and tongs to Zlatoličje HPP	10 days	Mon	Fri 21.03.25	17SS
21		**INSTALLATION, SETTING AND TESTING**	**50 days**	**Mon**	**Fri 30.05.25**	
22		Preparation works	3 days	Mon	Wed	20
23		Installation	10 days	Mon	Fri 4.04.25	20
24		Settings and tests	25 days	Mon 7.04.25	Fri 9.05.25	23
25		Repair of corrosion protection	15 days	Mon	Fri 30.05.25	24
26		**TESTS AND TRIAL OPERATION**	**139 days**	**Mon 2.06.25**	**Thu 11.12.25**	
27		Testing	49 days	Mon 2.06.25	Thu 7.08.25	25
28		Trial operation	90 days	Fri 8.08.25	Thu 11.12.25	27
29		**FINISHING WORKS**	**90 days**	**Fri 8.08.25**	**Thu 11.12.25**	
30		Dismantling the existing crane	15 days	Fri 5.09.25	Thu 25.9.25	18
31		Site clearance and cleaning	40 days	Fri 8.08.25	Thu 2.10.25	27
32		Handover of documentation	23 days	Tue 11.11.25	Thu 11.12.25	28ZZ
33		**CONTRACT CONCLUSION**	**0 days**	**Thu 11.12.25**	**Thu 11.12.25**
